

ZEFFERT & ASSOCIATES

Accessibility Site Visit (Master)

CONTACT INFORMATION

	<u>ZEFFERT & ASSOCIATES</u> 12101 Woodcrest Executive Drive Suite 180 St. Louis, MO 63141 Fred Donnell, Jr. - Manager, Inspection Services fdonnell@zeffert.com Office: 314.336.4869 Cell: 636.697.4151
--	--

PROJECT PROFILE

Project Name	Sample Property
Visit Type	1
Date of Inspection	01-15-2020
Inspector	Brian Jones
Site Visit Accompaniment	Kevin House/ Julio Perez
Next Action Required:	Physical Site Visit
City	Aiken
State	South Carolina
Number of Buildings	23
Total Number of Units	47
Number of HC Accessible Units	3
Number of A/V Units	1
General Project Notes:	NOTE – Element Findings at Time of Inspection: This inspection report indicates individual elements as Yes, No, or N/A. Each element listed as Yes is compliant and requires no action. Each element listed as No is not compliant and requires action. Each element listed as N/A is non-applicable and requires no action or not installed at the time of inspection.

Accessibility Site Visit (Master)

General Project Photos



ACCESSIBLE PARKING

Location of Parking	Throughout Property
HC Parking Status	Under Construction
Accessible Parking Photos	

Accessibility Site Visit (Master)

ACCESSIBLE ROUTE

Accessible Route Location	Throughout Property
Status of accessible route	Under Construction
Add Photos of Accessible Route	

COMMUNITY/COMMON AREAS

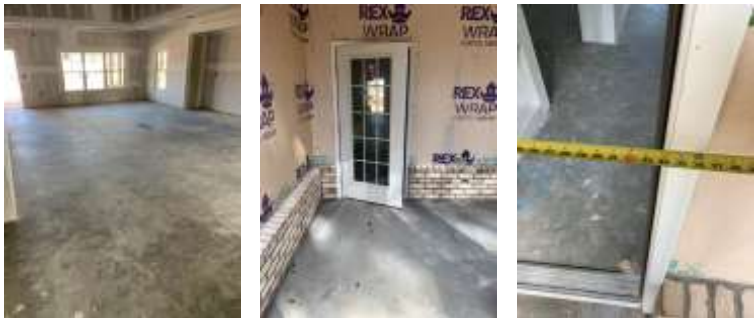
Community Kitchen

Status of this area	Drywall stage
Doorway has a clear opening width 32" min. (ADA 404.2.3)	Yes
Common Kitchen Photos	

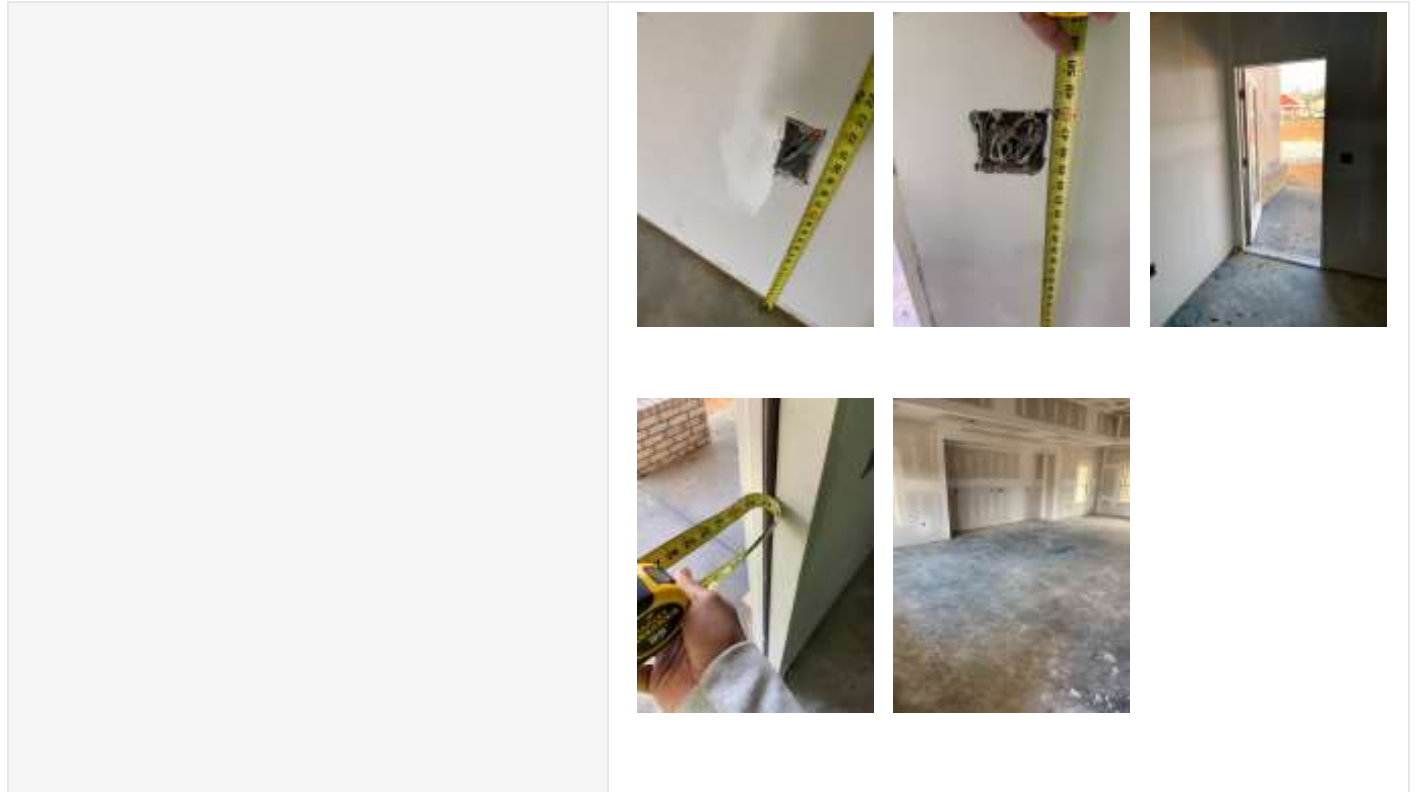
Accessibility Site Visit (Master)

	
--	--

Community Room

Status of this area	Drywall stage
Doorway has a clear opening width 32" min. (ADA 404.2.3)	Yes
Electric switches 48" max. AFF and outlets 15" min. (unobstructed) (ADA 308.2.1)	Yes
Community Room Photos	

Accessibility Site Visit (Master)



Computer Center

Location of this area	Community Building
Status of this area	Drywall stage
Doorway has a clear opening width 32" min. (ADA 404.2.3)	Yes
Electric switches 48" max. AFF and outlets 15" min. (unobstructed) (ADA 308.2.1)	Yes

Accessibility Site Visit (Master)

Computer Center Photos



Drinking Fountain

Location of drinking fountain	Community Building
Status of Drinking Fountain	Not installed
Drinking Fountain Photos	

Accessibility Site Visit (Master)

Fitness Center

Location of Fitness Center	Community Building		
Status of this area	Drywall stage		
Fitness Center Photos	    		

Leasing Office

Status of this area	Drywall stage
Doorway has a clear opening width 32" min. (ADA 404.2.3)	Yes
Electric switches 48" max. AFF and outlets 15" min. (unobstructed) (ADA 308.2.1)	Yes

Accessibility Site Visit (Master)

Leasing Office Photos



Other Community Area

Description of Community Area	Community Building
Doorway has a clear opening width 32" min. (ADA 404.2.3)	Yes
Electric switches 48" max. AFF and outlets 15" min.	Yes

Accessibility Site Visit (Master)

Other Community Area Photos

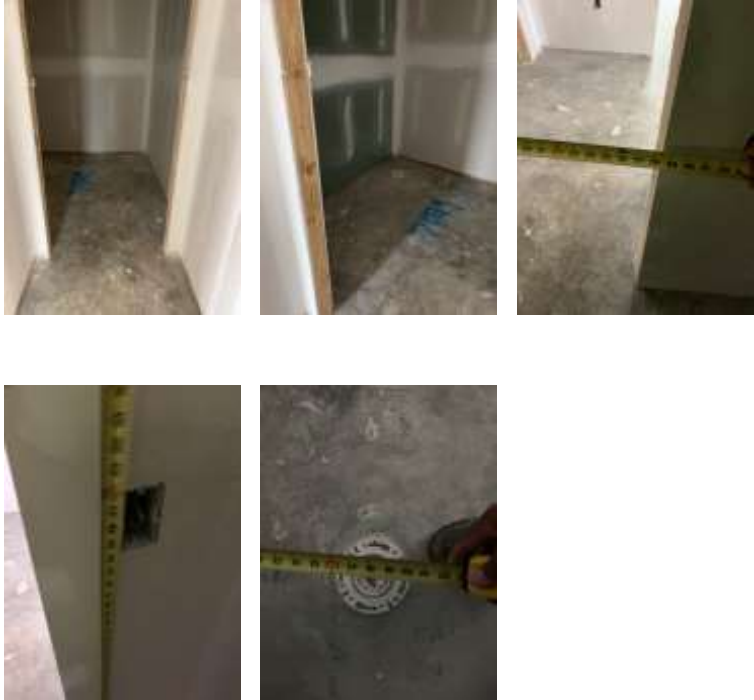


Public Restroom

Public Restroom Description	Community Building Men's
Status of this area	Drywall stage
Restroom Photos	  

Accessibility Site Visit (Master)

	
--	--

Public Restroom Description	Community Building Women's
Status of this area	Drywall stage
Doorway has a clear opening width 32" min. (ADA 404.2.3)	Yes
Restroom Photos	

Accessibility Site Visit (Master)

AV UNIT

AV Unit Misc.

Unit Number	Building 4 right side
Comments for AV Unit Misc.	Not framed only a slab
Photos for AV Unit Misc.	

HC UNIT

HC Unit Misc.

Unit Number	Building 23 right side
Number of HC Bedrooms (2 must meet compliance) (UFAS 4.34.2 c)	2
Type of shower/bath	Roll-in Shower
Primary Entrance - clear width 32" min. (UFAS 4.13.5)	Yes
Hall Closet - depth and door opening compliant (UFAS 4.13.5)	Yes
36" min width accessible route through dwelling unit (UFAS 4.34.2 (3), 4.3)	Yes
Comments for HC Unit Misc.	No electrical installed at the time of inspection

Accessibility Site Visit (Master)

Photos for HC Unit Misc.



Accessibility Site Visit (Master)

	
--	--

HC Unit Kitchen

Entry and/or door 32" min. (UFAS 4.13.5)	Yes
Additional Comments for HC Unit Kitchen	No electrical installed at the time of inspection
HC Unit Kitchen Photos	

HC - Bathroom Blocking

Status of Blocking	Framing stage
FHA & HC Units - All bathrooms required to have blocking. (UFAS 4.26, FHA 6.3)	In FHA & HC Units ALL bathrooms required to have blocking.

Accessibility Site Visit (Master)

Bathroom Blocking Photos



HC Unit Bathroom

Status of this area	Framing stage
HC Bathroom Photos	

HC Unit Laundry

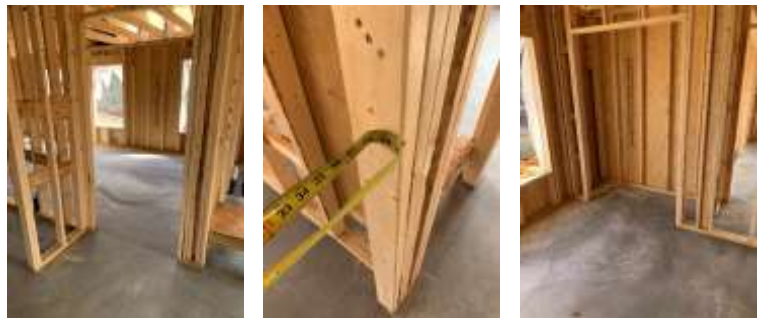
Status of this area	Framing stage
Doorway has a clear opening width 32" min. (UFAS 4.13.5)	Yes
Additional Comments for Laundry Area	No electrical installed at the time of inspection

Accessibility Site Visit (Master)

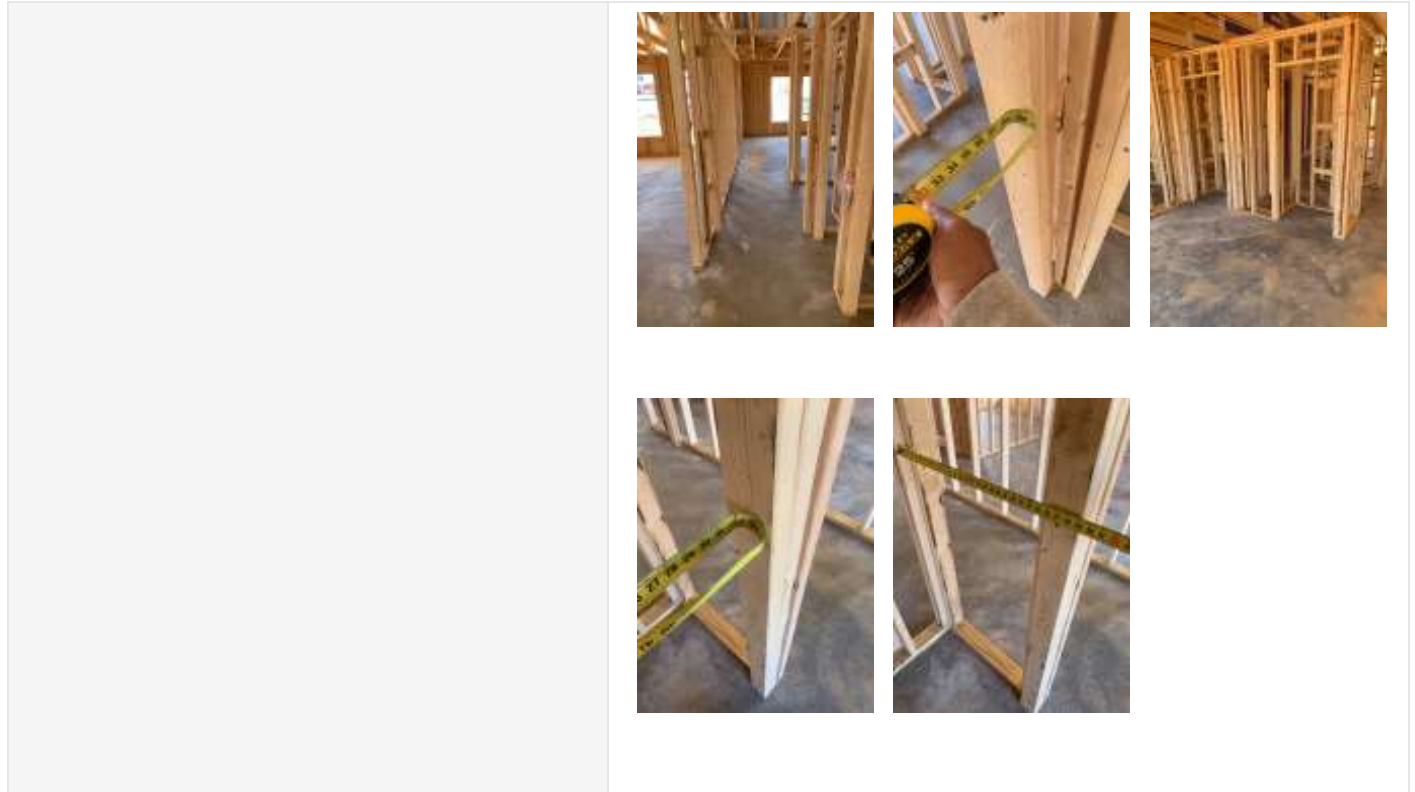
Laundry Area Photos



HC Unit BR

Bedroom Description	Bedrooms 1-2
Status of this area	Framing stage
Doorway has a clear opening width 32" min. (UFAS 4.13.5)	Yes
Closet - depth and door opening compliant (UFAS 4.13.5)	Yes
Additional Comments for HC Bedroom	No electrical installed at the time of inspection
HC Bedroom Photos	

Accessibility Site Visit (Master)

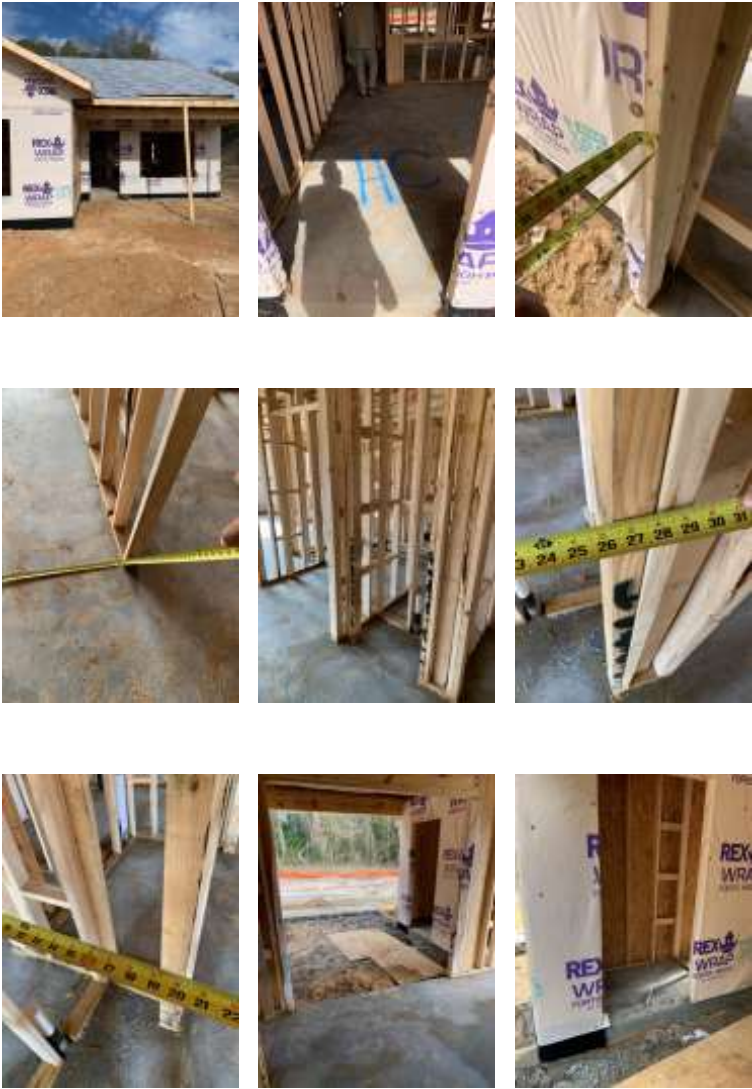


HC UNIT

HC Unit Misc.

Unit Number	Building 20 right side
Number of HC Bedrooms (2 must meet compliance) (UFAS 4.34.2 c)	2
Type of shower/bath	Roll-in Shower
Primary Entrance - clear width 32" min. (UFAS 4.13.5)	Yes
Secondary Entrance - clear width 32" min. (UFAS 4.13.5)	Yes
Storage Entrance - clear width 32" min. (UFAS 4.13.5)	Yes

Accessibility Site Visit (Master)

36" min width accessible route through dwelling unit (UFAS 4.34.2 (3), 4.3)	Yes
Comments for HC Unit Misc.	No electrical installed at the time of inspection
Photos for HC Unit Misc.	 The photographs provide a visual record of the construction progress for the accessible route. The top row shows the exterior of the building and the initial interior framing. The middle row shows close-up measurements of the route width, which is marked with blue paint on the concrete floor. The bottom row shows further framing and measurements, ensuring the route meets the required 36-inch minimum width.

Accessibility Site Visit (Master)

	
--	--

HC Unit Kitchen

Status of this area	Framing stage
Additional Comments for HC Unit Kitchen	No electrical installed at the time of inspection
HC Unit Kitchen Photos	

HC - Bathroom Blocking

Status of Blocking	Framing stage
FHA & HC Units - All bathrooms required to have blocking. (UFAS 4.26 FHA 6.3)	In FHA & HC Units ALL bathrooms required to have blocking.
2" x 8" blocking installed 32" - 38" AFF for length of 42" for 36" grab bar (UFAS Fig. 47)	Yes

Accessibility Site Visit (Master)

2" x 8" blocking installed 32" - 38" AFF for length of 54" for 42" grab bar (UFAS Fig. 47)	No
Bathtub or shower enclosure has 2" x 8" blocking installed 32" - 38" AFF on three walls (UFAS Fig. 48)	No
Bathroom Blocking Photos	

HC Unit Bathroom

Status of this area	Framing stage
----------------------------	----------------------

Accessibility Site Visit (Master)

HC Bathroom Photos



HC Unit Laundry

Status of this area	Framing stage
Doorway has a clear opening width 32" min. (UFAS 4.13.5)	Yes
Additional Comments for Laundry Area	No electrical installed at the time of inspection
Laundry Area Photos	

HC Unit BR

Bedroom Description	Bedrooms 1-2
Status of this area	Framing stage
Doorway has a clear opening width 32" min. (UFAS 4.13.5)	Yes

Accessibility Site Visit (Master)

Closet - depth and door opening compliant (UFAS 4.13.5)	Yes
Additional Comments for HC Bedroom	No electrical installed at the time of inspection
HC Bedroom Photos	     

HC UNIT

HC Unit Misc.

Unit Number	Building 8 right side
Comments for HC Unit Misc.	Not framed, only a slab

Accessibility Site Visit (Master)

Photos for HC Unit Misc.

